


ID	Task Name	Duration	Start	Finish	Predecessors	Aug '02				Sep '02				Oct
						4	11	18	25	1	8	15	22	29
1														
2	Config 1. Barrel Sector Tests	98 days	Wed Aug 14	Fri Dec 27										
3	Thermal Tests	13 days	Wed Aug 14	Fri Aug 30										
4	Exhaust diameter upgrade	2 days	Mon Sep 2	Tue Sep 3	3									
5	Flow Meter Installation	2 days	Wed Sep 4	Thu Sep 5	4									
6	Heater Installation	1 day	Fri Sep 6	Fri Sep 6	5									
7	Capacitive Tests	21 days	Mon Sep 9	Mon Oct 7	6									
8	Rebuild Sector in Freezer	23 days	Tue Oct 8	Thu Nov 7	7									
9	Repeat ALL tests	36 days	Fri Nov 8	Fri Dec 27	8									
10														
11	Establish Freezer Operation	6 days	Wed Aug 14	Wed Aug 21										
12	Build Freezer support trolley	1 day	Wed Aug 14	Wed Aug 14										
13	Registration	1 day	Thu Aug 15	Thu Aug 15	12									
14	Seal Edges	1 day	Fri Aug 16	Fri Aug 16	13									
15	Inset Dew Point Meter	1 day	Mon Aug 19	Mon Aug 19	14									
16	Flood with Nitrogen	1 day	Tue Aug 20	Tue Aug 20	15									
17	Test seals and measure dew point	1 day	Wed Aug 21	Wed Aug 21	13,14,15,11									
18	Finalization of Freezer Commissioning	8 days	Thu Aug 22	Mon Sep 2	17									
19	Design New lid	1 day	Thu Aug 22	Thu Aug 22	17									
20	Design Camera Trolley	1 day	Fri Aug 23	Fri Aug 23	19									
21	Build Camera Trolley	1 day	Mon Aug 26	Mon Aug 26	20									
22	Design Servies Support	3 days	Tue Aug 27	Thu Aug 29	21									
23	Assemble and Test W/O BSP	1 day	Fri Aug 30	Fri Aug 30	22									
24	Installation of CAL controller	1 day	Mon Sep 2	Mon Sep 2	23									
25														
26	Upgrade BSP to config 2	19 days	Tue Oct 8	Fri Nov 1										
27	Strip down config 1	1 day	Tue Oct 8	Tue Oct 8	7									
28	Install new brackets	3 days	Wed Oct 9	Fri Oct 11	27									
29	Upgrade and install dummies	4 days	Mon Oct 14	Thu Oct 17	28									
30	Metrology of sector	2 days	Fri Oct 18	Mon Oct 21	29									
31	Installation of New Cooling Loop	2 days	Tue Oct 22	Wed Oct 23	30									
32	Install clips	1 day	Thu Oct 24	Thu Oct 24	31									
33	Additional Instrumentation	2 days	Fri Oct 25	Mon Oct 28	32									

Project: BSP.Phase2 Date: Thu Aug 15	Task		Rolled Up Task		Project Summary	
	Split		Rolled Up Split		External Milestone	
	Progress		Rolled Up Milestone		Deadline	
	Milestone		Rolled Up Progress			
	Summary		External Tasks			

ID	Task Name	Duration	Start	Finish	Predecessors	g '02				Sep '02				Oct
						4	11	18	25	1	8	15	22	29
34	Cable routing an installation	2 days	Tue Oct 29	Wed Oct 30	33									
35	Electrical Module Installation	2 days	Thu Oct 31	Fri Nov 1	34									
36														
37	Related activities	6 days	Tue Sep 3	Tue Sep 10										
38	Freezer software	1 day	Tue Sep 3	Tue Sep 3	24									
39	Power Supply Software	1 day	Wed Sep 4	Wed Sep 4	38									
40	New temp sensor software	1 day	Thu Sep 5	Thu Sep 5	39									
41	Receive irradiated module	1 day	Fri Sep 6	Fri Sep 6	40									
42	Risk assesment for irrad module	1 day	Mon Sep 9	Mon Sep 9	41									
43	Complete Thero Mech'l Modules	1 day	Tue Sep 10	Tue Sep 10	42									
44														
45														
46														
47	Barrel 3 Schedule	104 days	Wed Oct 23	Mon Mar 17										
48	B3 arrives at RAL	1 day	Fri Nov 29	Fri Nov 29										
49	Harness Delivery	1 day	Fri Dec 20	Fri Dec 20										
50	Cooling Loop Delivery	1 day	Wed Oct 23	Wed Oct 23										
51	Fitting Barrel 3	60 days	Mon Dec 23	Fri Mar 14	49,50									
52	Barrel 3 to Oxford	1 day	Mon Mar 17	Mon Mar 17	51									


Project: BSP.Phase2
Date: Thu Aug 15

Task		Rolled Up Task		Project Summary	
Split		Rolled Up Split		External Milestone	
Progress		Rolled Up Milestone		Deadline	
Milestone		Rolled Up Progress			
Summary		External Tasks			

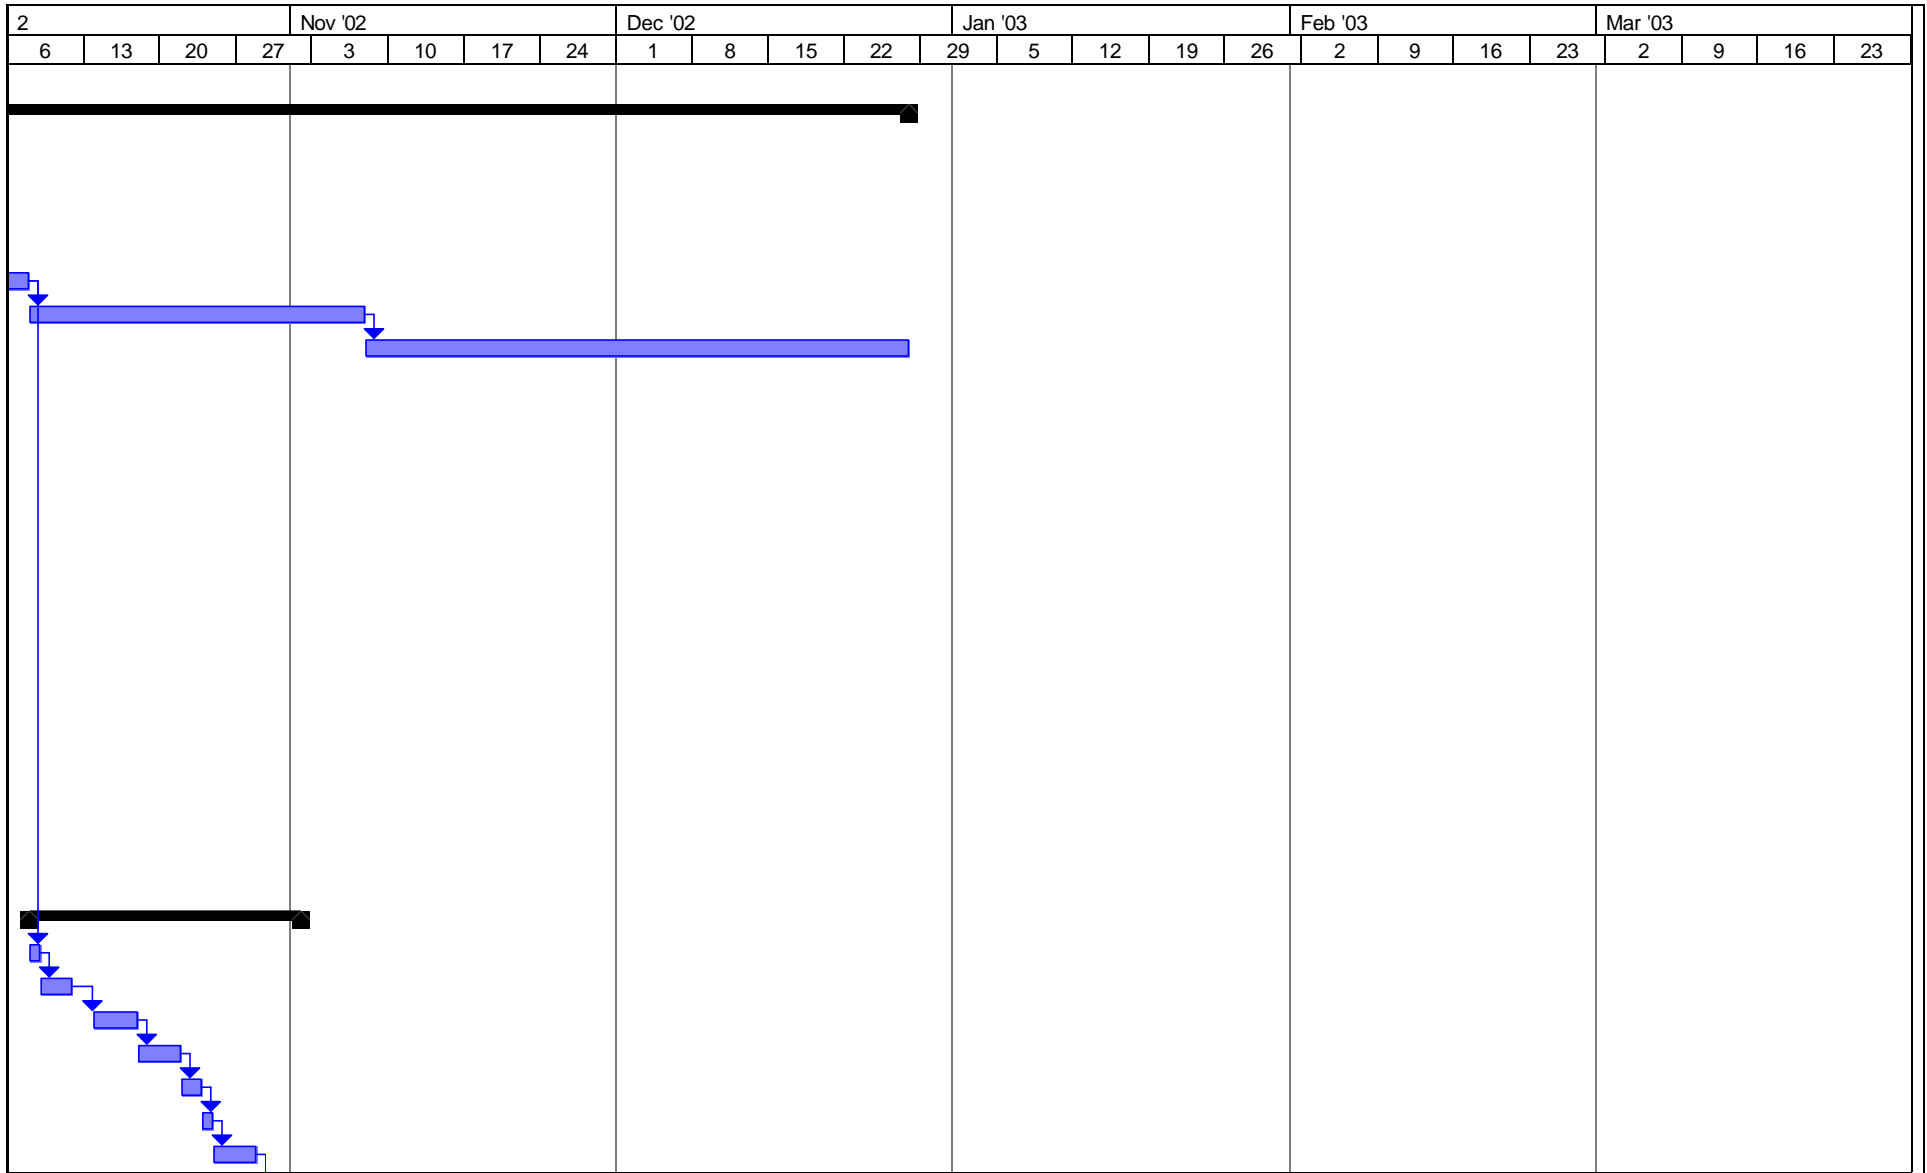

Project: BSP.Phase2
Date: Thu Aug 15

Task		Rolled Up Task		Project Summary	
Split		Rolled Up Split		External Milestone	
Progress		Rolled Up Milestone		Deadline	
Milestone		Rolled Up Progress			
Summary		External Tasks			

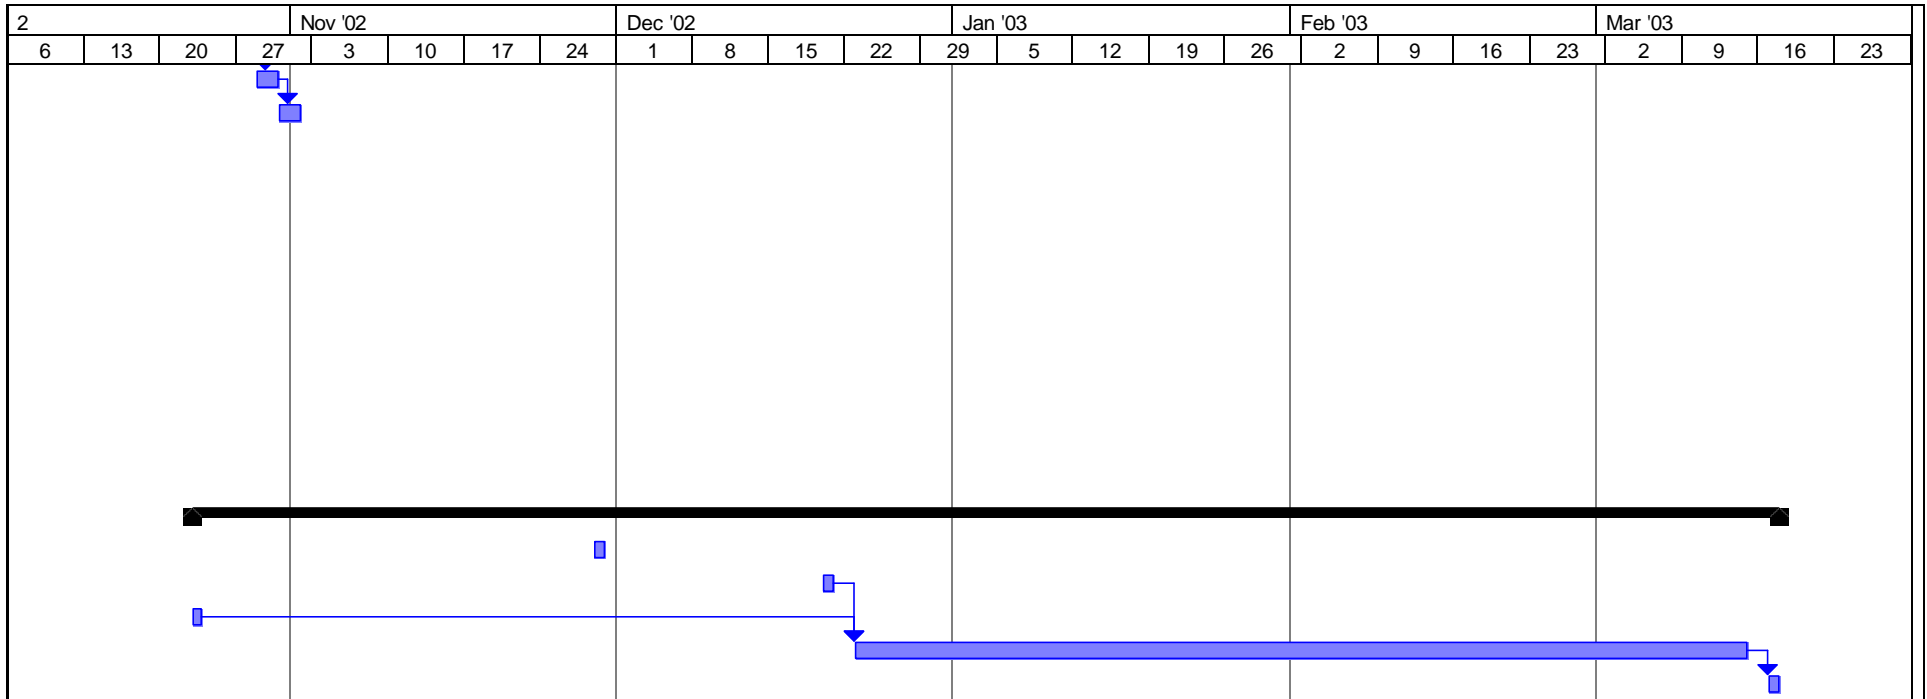

Project: BSP.Phase2
Date: Thu Aug 15

Task		Rolled Up Task		Project Summary	
Split		Rolled Up Split		External Milestone	
Progress		Rolled Up Milestone		Deadline	
Milestone		Rolled Up Progress			
Summary		External Tasks			
